

PROJECT PLANNING PHASE

Incident Lifecycle Automation in ServiceNow

Date 08 September 2026

Team ID _____

Project Name Incident Lifecycle Automation in ServiceNow

Maximum Marks 5 Marks

1. Planning Approach

The project is planned using Agile/Scrum concepts. Large functional areas are treated as Epics, and each Epic is divided into User Stories (USN). Story Points use the Fibonacci-style values 1, 2, 3 and 5 to estimate relative effort. The backlog below is a project-planning estimate; actual completion values should be updated after execution.

2. Product Backlog, Sprint Schedule and Estimation

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Service & Incident Setup	USN-1	As a Service Desk Agent, I can create a Service and Service Offering so that incidents can be associated with the correct service.	3	High	_____
Sprint-1	Incident Management	USN-2	As a Service Desk Agent, I can create an Incident Record with the required incident information.	3	High	_____
Sprint-1	Incident Classification	USN-3	As a Service Desk Agent, I can classify an incident using Category, Subcategory, Urgency, Service and Configuration Item.	3	High	_____
Sprint-1	Knowledge & Agent Assist	USN-4	As a Service Desk Agent, I	3	High	_____

			can use Knowledge Management and Agent Assist to find relevant troubleshooting information.			
Sprint-1	Assignment & Escalation	USN-5	As a Service Desk Agent, I can reassign or escalate an incident to the appropriate support group when required.	3	High	_____
Sprint-2	Level 2 Support	USN-6	As a Level 2 Technician, I can investigate an escalated incident and track the investigation details.	3	High	_____
Sprint-2	Change Management	USN-7	As a support stakeholder, I can create and relate an Emergency Change Request when an incident requires urgent change activity.	3	Medium	_____
Sprint-2	Parent/Child Incidents	USN-8	As a Service Desk Agent, I can create and relate a Child Incident so that recurring or related issues can be tracked.	3	Medium	_____
Sprint-2	Resolution & Closure	USN-9	As a Service Desk Agent, I can document Cause, Resolution, Resolution Details and closure information before resolving/closing the incident.	3	High	_____
Sprint-2	Knowledge Management	USN-10	As a support stakeholder, I can create a Knowledge	3	Medium	_____

			Article from useful resolution information for future incidents.			
Sprint-2	Validation & Testing	USN-11	As a project team member, I can validate the incident, service, SLA, change, child incident, knowledge and related records and perform deployment testing.	5	High	

Total planned story points: 35 (Sprint-1 = 15; Sprint-2 = 20).

3. Sprint Schedule

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	15	6 Days	08 Sep 2026	13 Sep 2026	To be recorded	To be recorded
Sprint-2	20	6 Days	15 Sep 2026	20 Sep 2026	To be recorded	To be recorded

4. Velocity Calculation

Planned total story points = 15 + 20 = 35.

Number of planned sprints = 2.

Planned average velocity = Total Story Points / Number of Sprints = 35 / 2 = 17.5 story points per sprint.

For a 6-day sprint, the planned average rate is approximately 17.5 / 6 = 2.92 story points per day.

Note: This is a planning velocity based on the estimated backlog. Actual team velocity should be calculated from story points completed after the sprints.


5. Project Tracker

Epic	User Stories	Planned Points	Sprint	Status
Service & Incident Setup	USN-1, USN-2	6	Sprint-1	Planned
Incident Classification	USN-3	3	Sprint-1	Planned
Knowledge & Agent Assist	USN-4	3	Sprint-1	Planned
Assignment & Escalation	USN-5	3	Sprint-1	Planned
Level 2 Support	USN-6	3	Sprint-2	Planned
Emergency Change	USN-7	3	Sprint-2	Planned
Child Incident	USN-8	3	Sprint-2	Planned
Resolution & Closure	USN-9	3	Sprint-2	Planned
Knowledge Article	USN-10	3	Sprint-2	Planned

Validation & Testing	USN-11	5	Sprint-2	Planned
----------------------	--------	---	----------	---------

6. Planned Burndown Chart

The chart below is a planned burndown for the 35-point backlog. It represents expected remaining work over the two 6-day sprints and is not an actual execution result.

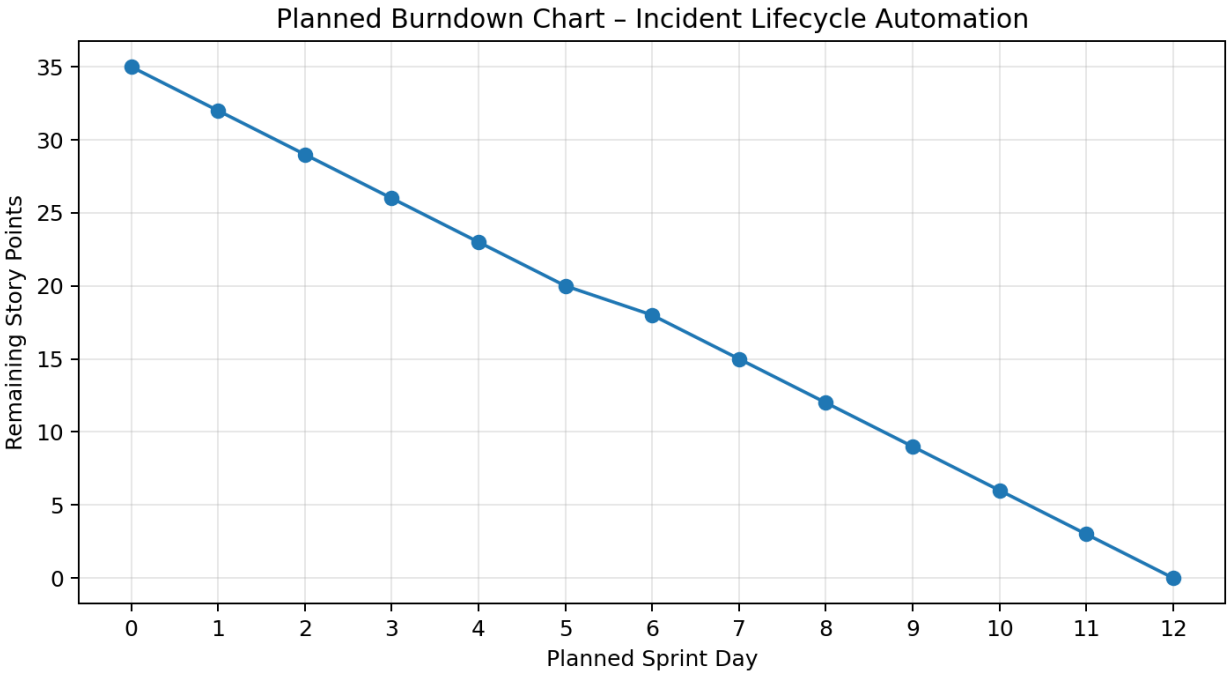

7. Planning Summary

The backlog covers the complete Incident Lifecycle Automation workflow: service and service offering setup, incident creation and classification, knowledge-assisted troubleshooting, escalation to Level 2, emergency change linkage, child incidents, resolution and closure, knowledge article creation, and final validation/testing. Sprint-1 focuses on setup and core incident handling, while Sprint-2 completes advanced lifecycle activities and validation.
